8-Week Project Plan — Windsor Housing Visual Analytics

Oct 7, 2026 · @dhriti

How the work is divided

Every member works 22 hours a week for 8 weeks (Oct 8 – Dec 3), about 176 hours each, and every member does technical work every week. The split rests on four rules:

- **Own a story end to end.** Each member owns one housing story from raw file to ETL, SQL views, Superset dashboard, React page, narrative and report section. Nobody is "only research" or "only coding".
- **Own one platform piece too.** Each member also owns one shared technical component: the ETL framework, Superset/Docker, the React site, or hosting and CI.
- **Review each other's work.** Code reviews and number checks rotate across members, so every piece is checked by someone who did not build it.
- **Same weekly load.** Weekly hours sit at 22 for everyone, which leaves 2 hours of slack above the 20-hour minimum. Technical work is 52–56% of every member's hours, and the weekly supervisor status note rotates so coordination does not crowd out anyone's technical work.

Task types in the tables: **Tech** = code, SQL, dashboards, deployment; **Research** = data audits, analysis, validation, testing; **Docs** = narrative, report, slides; **PM** = planning and coordination. Week 1 starts on Oct 8, the day of the proposal presentation, and Week 8 ends on Dec 3 with the final demo.

Sprint backlogs, scrum meetings and the project manager's review duties:
Sprints and Scrum

Who owns what

Each row is one person's full slice of the project: a story, a platform component and a coordination role.

Member	Story owned end to end	Main dataset	Platform piece	Also leads
Dhritiben Patel	Story 1: Who faces the greatest affordability pressure?	StatsCan 98-10-0252-01 (shelter-cost-to-income)	Hosting, deployment, GitHub Actions CI	Project management, supervisor contact, final report assembly
Romit Patel	Story 2: What is happening in Windsor's rental market (2015–2025 trends)?	CMHC Rental Market Survey, Windsor 2025 + historical workbooks	PostgreSQL schema, shared ETL framework, data quality, refresh pipeline	Data dictionary, reproducibility and code submission
Pavan Rella	Story 4: How does Windsor compare? + affordability-gap index	CMHC RMS Canada 2025; 2021 Census Profile	Superset + Docker setup, KPI catalogue, dashboard standards	Findings write-up, Q&A preparation
Charmiben Patel	Story 3: What does housing supply look like?	CMHC starts/completions (2015–2025)	React website, Superset embedding	Slide design, demo script and backup recording

Compared with the proposal's role table, Dhritiben now owns hosting, CI, production fixes, load testing and the reproducibility test, so her technical load matches everyone else's. Report assembly, the user-testing plan and the weekly status note are shared across the team.

Timeline and checkpoints

Eight weeks from data audit to the final demo on Dec 3



8-week roadmap · 4 phases, 4 checkpoints

The hosting test in Week 2 is the early go/no-go for free deployment; code freezes on Nov 27 so Week 8 is only report, slides, submission and demo.

Week-by-week tasks

Weeks run Thursday to Wednesday so that sprint planning follows each Wednesday review; Week 8 runs one extra day to Thursday, Dec 3. Each task lists what it produces, so its hours can be checked. Estimates are at student pace and include time to learn tools that are new to the team (Superset, Docker, embedding).

Week 1 · Oct 8–14 — Data audit and foundations

Shared by all: 2h team meetings and 2h for the proposal presentation on Oct 8. Each member's rows add up to 18h, for 22h in total. Already done before Week 1: Jira board and all datasets found and downloaded.

Member	Task	What it covers	Hours	Type
Dhritiben	Profile the shelter-cost table (98-10-0252-01)	Notebook listing every category of the 4 dimensions (income band, household type, tenure, cost-to-income band); check that sub-totals add up to totals across the 2,389 rows; count suppressed cells; 1-page audit note	5h	Research
Dhritiben	Shared StatsCan profiling module	Reusable Python functions every member uses: read CSVs with the right encoding, detect symbol values (x, F, ..), summarise nulls and ranges per column; tested on 2 files	5h	Tech
Dhritiben	Prototype the wide-to-long reshape	pandas script that turns the table into one row per income × household × tenure × cost band; check the row count against the expected number of combinations	3h	Tech
Dhritiben	Compare free hosting options	Oracle Cloud Free, Render, Railway and a university server compared on RAM, storage, sleep rules and cost; recommendation for the Week 2 hosting test	2h	Research
Dhritiben	Story 1 questions and measures	4–6 questions, each mapped to exact table columns and the formula that answers it	2h	Docs

Member	Task	What it covers	Hours	Type
Dhritiben	Week 1 acceptance review	Check every Week 1 ticket against its acceptance criteria before the Oct 14 review; accepted/returned list	1h	PM
Romit	Repository and dev environment	GitHub repo with branch protection, folders (raw, staging, etl, sql, web), requirements file, pre-commit hooks; get all 4 laptops running it	3h	Tech
Romit	Profile the CMHC Windsor RMS 2025 workbook	Go through all 29 sheets: header layout, units, zones, bedroom types, reliability letters and ** markers; pick the 8–10 sheets the stories need; sheet catalogue	6h	Research
Romit	Raw staging load	Python script that loads every raw CSV and sheet as-is into a staging schema, tagged with file name and load date; safe to re-run	5h	Tech
Romit	Conceptual ER model	Dimensions (geography, period, tenure, income band, household type, bedroom type, zone, dwelling type) and one fact table per source; reviewed with Pavan	4h	Tech
Pavan	Docker setup for PostgreSQL + Superset	Compose file with PostgreSQL, Superset and Redis, admin init script, persistent volumes; tested on Windows and Mac; written setup guide	6h	Tech

Member	Task	What it covers	Hours	Type
Pavan	Census Profile extraction script	Python script that reads the 98-401 CSV, keeps Windsor CMA, selects ~60 characteristics (population, income, tenure, shelter cost) and writes a clean file	5h	Tech
Pavan	Choose comparator CMAs	Pick 4–5 Ontario CMAs comparable to Windsor by size and market; confirm each has the same RMS 2025 tables; short justification	3h	Research
Pavan	End-to-end test chart	Connect Superset to the staging data and build one chart to prove the whole stack works	2h	Tech
Pavan	Data dictionary: census and comparison	Every kept column with meaning, unit, source table and year	2h	Docs
Charmiben	React project scaffold	Vite + React app, React Router with 6 routes (home, 4 stories, methodology), ESLint and Prettier, preview build	4h	Tech
Charmiben	Layout and navigation shell	Header, footer, responsive menu, page container, shared colours and type; checked on phone width	4h	Tech
Charmiben	Profile the CMHC starts/completions workbook	Find the Windsor tables, list dwelling types, monthly vs annual series and years covered; check totals; audit note	5h	Research

Member	Task	What it covers	Hours	Type
Charmiben	Website wireframes	Low-fidelity wireframes for home, a story page with an embedded dashboard, and methodology; reviewed in the team meeting	3h	Docs
Charmiben	Data dictionary: supply tables	Every kept column with meaning, unit and source	2h	Docs

Week 2 · Oct 15–21 — ETL framework and database

Shared by all: 2h team meetings. Each member's rows add up to 20h, for 22h in total.

Member	Task	What it covers	Hours	Type
Dhritiben	Affordability ETL (production)	Turn the prototype into a framework job: symbols to NULL plus a flag column, standard category labels, load into the fact table, log row counts	8h	Tech
Dhritiben	Hosting test on a free VM	Create the VM, install Docker, run the Superset + PostgreSQL stack with sample data, measure memory and page load; go/no-go note	5h	Tech
Dhritiben	Unit tests for the affordability ETL	pytest cases for symbol handling, row counts and totals matching the raw file	3h	Tech
Dhritiben	Sprint 1 acceptance review and status note	Check each member's Sprint 1 items against the definition of done; 1-page status note to the supervisor	2h	PM

Member	Task	What it covers	Hours	Type
Dhritiben	Story 1 narrative outline	Flow of the story page: question, 3–4 findings to test, chart order	2h	Docs
Romit	Shared ETL framework	Config file per dataset; loader that validates the schema and stops on unexpected columns; logging; load-audit table (file, rows, time, status)	8h	Tech
Romit	PostgreSQL schema	DDL for all dimension and fact tables with keys, constraints and indexes; ER diagram exported for the report	6h	Tech
Romit	ETL: CMHC RMS 2025 core sheets	Vacancy, average rent, rental universe and turnover by bedroom type and zone into fact tables; reliability letter kept as a column	5h	Tech
Romit	Code review: affordability ETL	Review Dhritiben's pull request	1h	Tech
Pavan	ETL: Census Profile subset	Load the ~60 characteristics through the framework; check against the published profile (population 422,630)	5h	Tech
Pavan	Superset configuration	Database connection, roles, a Public role, and a test of anonymous viewing	4h	Tech
Pavan	Embedding research	Superset Embedded SDK with guest tokens vs public dashboards: security, setup effort, hosting needs; recommendation	4h	Research

Member	Task	What it covers	Hours	Type
Pavan	KPI catalogue	15–20 KPIs across the 4 stories, each with definition, formula, source table, unit and caveat	4h	Docs
Pavan	Code review: PostgreSQL schema	Check keys, data types and naming; run test inserts	3h	Tech
Charmiben	ETL: starts and completions	Reshape the workbook into long format (year, month, dwelling type, measure), load through the framework, check totals	7h	Tech
Charmiben	Story-page template and methodology page	Reusable story component (question, narrative blocks, dashboard slot, source line) and a methodology page with source links	6h	Tech
Charmiben	Embedding spike (with Pavan)	Embed one test dashboard in React with @superset-ui/embedded-sdk and a guest token; list blockers	4h	Tech
Charmiben	Profile 2015–2025 starts history	Check older editions for dwelling-type naming changes; mapping table	3h	Research

Week 3 · Oct 22–28 — All data loaded, analytical SQL views

Shared by all: 2h team meetings. Each member's rows add up to 20h, for 22h in total.

Member	Task	What it covers	Hours	Type
Dhritiben	SQL views for Story 1	Views for burden rate by income band, by household type and owner vs renter, with counts and percentages; tested against raw totals	6h	Tech
Dhritiben	GitHub Actions CI + hosting decision	Lint and pytest on every pull request, required check on main; 1-page hosting decision from the Week 2 test	5h	Tech
Dhritiben	Validate Story 1 against published figures	Reproduce StatsCan's published figures (34.8% of tenants and 10.9% of owners at 30%+) from the database; log any differences	3h	Research
Dhritiben	Code review: data-quality checks	Review Romit's validation pull request and run it locally	3h	Tech
Dhritiben	Story 1 chart list and narrative v1	Chart-by-chart plan and a first draft of the story text	3h	Docs
Romit	ETL: historical RMS 2015–2024	Load 10 years of Windsor workbooks into the same fact tables; map renamed or redrawn zones to 2025 zones; flag years with breaks	9h	Tech
Romit	Automated data-quality checks	Row counts vs source, rent and vacancy ranges, duplicate keys, reliability letters; validation report produced on every load	5h	Tech
Romit	SQL views for Story 2	Rent year-over-year change, 10-year growth rate, vacancy trend, turnover by bedroom type	5h	Tech

Member	Task	What it covers	Hours	Type
Romit	ETL README	How to run, add a dataset and read the load-audit table	1h	Docs
Pavan	ETL: RMS Canada comparison data	Rent and vacancy for Windsor and the chosen CMAs into the same fact tables	5h	Tech
Pavan	Design the affordability-gap index	Define rent growth vs renter income growth, test on Windsor and comparators, write a method note with limits	5h	Research
Pavan	SQL views for Story 4	Windsor vs comparator rents, vacancy and index values	4h	Tech
Pavan	Register Superset datasets and theme	Add every view as a dataset with saved metrics; one shared colour palette	4h	Tech
Pavan	Weekly supervisor status note (rotating)	Collect progress from all 4 members and send the note	2h	PM
Charmiben	SQL views for Story 3	Starts and completions by dwelling type per year; supply per 1,000 households using census households	6h	Tech
Charmiben	React home and data-sources pages	Home page with intro and 4 story cards; sources page with each dataset's link, release date and licence; responsive	6h	Tech
Charmiben	Data-quality checks for supply tables	Counts, ranges and missing months, added to the shared validation report	4h	Tech
Charmiben	Story 3 narrative v1	First draft of the story text	3h	Docs

Member	Task	What it covers	Hours	Type
Charmiben	Peer test: affordability ETL	Run Dhritiben's ETL on a clean database and report problems	1h	Tech

Week 4 · Oct 29–Nov 4 — First dashboards and supervisor progress review

Shared by all: 2h team meetings. Each member's rows add up to 20h, for 22h in total.

Member	Task	What it covers	Hours	Type
Dhritiben	Story 1 Superset dashboard	6–8 charts: KPI tiles, burden by income band, renter vs owner, household-type breakdown, native filters for tenure and household type	8h	Tech
Dhritiben	Deploy first build to the host	Run the database and Superset on the chosen host with Story 1 data; share the link with the team	4h	Tech
Dhritiben	Exploratory analysis: Story 1	Query the views for patterns; write 3–5 findings, each with its number	4h	Research
Dhritiben	Progress review deck	Slides for the supervisor progress review (sprint review)	2h	Docs
Dhritiben	Sprint 2 acceptance review	Check every member's Sprint 2 items against the definition of done before the supervisor review; list rework	2h	PM
Romit	Story 2 Superset dashboard	Rent by bedroom type and zone, 10-year rent and vacancy trends, turnover, with filters	9h	Tech

Member	Task	What it covers	Hours	Type
Romit	One-command refresh	A single command re-runs every load in order and is safe to run twice; tested by doing so	5h	Tech
Romit	Exploratory analysis: Story 2	3–5 findings on rent and vacancy trends, each with its number	4h	Research
Romit	Progress review: pipeline section	Slides on the ETL flow and data checks	2h	Docs
Pavan	Story 4 Superset dashboard	Windsor vs comparator CMAs on rent, vacancy and the affordability-gap index	8h	Tech
Pavan	Exploratory analysis: Story 4	3–5 comparison findings, each with its number	4h	Research
Pavan	Filter and cross-filter standards	Shared rules for filter names, placement and defaults; applied to Story 1 as the example	3h	Tech
Pavan	Hosted Superset tuning	Caching, Redis and memory settings on the VM so dashboards load reliably	3h	Tech
Pavan	Progress review: dashboards section	Slides on the KPI catalogue and dashboards	2h	Docs
Charmiben	Story 3 Superset dashboard	Starts vs completions by dwelling type, supply per 1,000 households, year filter	8h	Tech
Charmiben	Embedding prototype	Small backend endpoint that issues guest tokens; Story 1 dashboard embedded in its React page	7h	Tech
Charmiben	Exploratory analysis: Story 3	3–5 supply findings, each with its number	3h	Research

Member	Task	What it covers	Hours	Type
Charmiben	Progress review: website section	Slides and a short demo of the site	2h	Docs

Week 5 · Nov 5–11 — Dashboards final, story pages in React

Shared by all: 2h team meetings. Each member's rows add up to 20h, for 22h in total.

Member	Task	What it covers	Hours	Type
Dhritiben	Production hardening	HTTPS certificate, secrets in environment variables, daily database backup job, firewall rules	5h	Tech
Dhritiben	React Story 1 page	Intro, question, 3 narrative blocks, embedded dashboard and source line	5h	Tech
Dhritiben	Refine Story 1 dashboard	Apply supervisor review comments; fix labels and units; add notes where data is suppressed	4h	Tech
Dhritiben	Final Story 1 narrative	About 600 words of finished story text	4h	Docs
Dhritiben	Data dictionary and decision log	Bring both up to date for all tables and design decisions	2h	Docs
Romit	React Story 2 page	Intro, narrative blocks, embedded dashboard and source line	5h	Tech
Romit	Scheduled refresh with schema guard	Weekly job that re-runs the pipeline and stops with an alert if a source file's columns change	5h	Tech
Romit	Refine Story 2 dashboard	Apply review comments; fix labels, units and filter defaults	4h	Tech

Member	Task	What it covers	Hours	Type
Romit	Final Story 2 narrative	About 600 words of finished story text	4h	Docs
Romit	Weekly supervisor status note (rotating)	Collect progress from all 4 members and send the note	2h	PM
Pavan	Refine Story 4 + KPI consistency check	Check that each KPI shows the same number on every dashboard; fix mismatches	6h	Tech
Pavan	React Story 4 page	Intro, narrative blocks, embedded dashboard and source line	5h	Tech
Pavan	Final Story 4 narrative	About 600 words of finished story text	4h	Docs
Pavan	Superset performance	Cache settings and indexes for the slowest views; measure load times before and after	3h	Tech
Pavan	Methodology page draft	Sources, year rules, suppression handling and limits, in plain language	2h	Docs
Charmiben	Embed all dashboards	Secure the guest-token endpoint; embed all 4 dashboards with loading and error states	8h	Tech
Charmiben	React Story 3 page	Intro, narrative blocks, embedded dashboard and source line	5h	Tech
Charmiben	Final Story 3 narrative	About 500 words of finished story text	3h	Docs
Charmiben	Mobile layout fixes	Make every page and embedded dashboard usable at phone width	2h	Tech

Member	Task	What it covers	Hours	Type
Charmiben	Accessibility check	Contrast, keyboard navigation and alt text checked with an automated tool plus a manual pass	2h	Research

Week 6 · Nov 12–18 — Live deployment, QA, report sections

Shared by all: 2h team meetings. Each member's rows add up to 20h, for 22h in total.

Member	Task	What it covers	Hours	Type
Dhritiben	Full live deployment	Deploy database, Superset and React to the host; run a smoke-test checklist on every page	8h	Tech
Dhritiben	Fix live embedding and deployment issues	CORS, guest-token and configuration problems that only appear on the live site	4h	Tech
Dhritiben	Code review: embedding code	Review Charmiben's endpoint and embed components, with a security focus	2h	Tech
Dhritiben	Report: management and methodology	About 4 pages: approach, sprint process, data rules	4h	Docs
Dhritiben	Sprint 3 acceptance review	Check every member's Sprint 3 items against the definition of done; confirm the live site passes the smoke test	2h	PM
Romit	Traceability check	For every KPI on the 4 dashboards, trace view → table → raw file row; about 40 checks in a tracking sheet	6h	Research

Member	Task	What it covers	Hours	Type
Romit	End-to-end pipeline tests	Automated test that builds the whole database from raw files on an empty instance	5h	Tech
Romit	Fix data issues from QA	Correct every problem the traceability check and peer QA found	4h	Tech
Romit	Report: pipeline and database	About 5 pages with ER diagram, ETL flow and validation approach	5h	Docs
Pavan	Fix Superset issues in production	Permissions, slow queries and caching problems on the live host	5h	Tech
Pavan	Dashboard consistency pass	Same colours, titles, units and filter placement across all 4 dashboards	5h	Tech
Pavan	Report: analysis and findings	About 5 pages: findings per story with charts	5h	Docs
Pavan	Peer QA: Stories 1 and 2	Recompute key numbers from the raw files and check filters	3h	Research
Pavan	Code review: React pages	Review the story-page pull requests	2h	Tech
Charmiben	Front-end polish	About/team page, page titles and meta tags, cross-browser test in Chrome, Firefox, Safari and Edge	6h	Tech
Charmiben	User-testing plan	Script of 6–8 tasks, feedback form, and 5–6 testers recruited and scheduled	4h	Docs

Member	Task	What it covers	Hours	Type
Charmiben	Report: implementation and front end	About 5 pages: site structure, embedding, deployment	5h	Docs
Charmiben	Peer QA: Story 4 and whole site	Check numbers, links and every page	3h	Research
Charmiben	Front-end README	How to run, build and deploy the site	2h	Docs

Week 7 · Nov 19–25 — User testing, fixes, report draft

Shared by all: 2h team meetings. Each member's rows add up to 20h, for 22h in total.

Member	Task	What it covers	Hours	Type
Dhritiben	Fix Story 1 issues from testing	Apply the user-testing fixes for the Story 1 page and dashboard	4h	Tech
Dhritiben	Monitoring and backup-restore test	Uptime monitor; restore last night's backup into a fresh database and confirm it works	4h	Tech
Dhritiben	Load test of the public site	Simulate concurrent visitors with a load-testing tool; record response times	3h	Tech
Dhritiben	Live refresh demo	Run the refresh on a newer source file end to end; screen-record it for the demo	3h	Tech
Dhritiben	User-testing sessions (half)	Run 3 sessions of about 45 minutes and write up notes	3h	Research
Dhritiben	Report draft: sections 1–4	Merge the introduction, background, methodology and pipeline sections into one draft	3h	Docs

Member	Task	What it covers	Hours	Type
Romit	Fix pipeline and data bugs	Correct problems found during user testing	5h	Tech
Romit	User-testing sessions (half) and feedback list	Run 3 sessions, then merge all 6 sessions into one prioritised issue list	5h	Research
Romit	README, architecture doc and setup guide	Final repository documentation a new student could follow	5h	Docs
Romit	Limitations and future work	Report section on data limits and possible extensions	3h	Docs
Romit	Code cleanup	Remove dead code, add comments and docstrings	2h	Tech
Pavan	Apply testing feedback to dashboards	Changes to labels, filters and chart choices that testers stumbled on	6h	Tech
Pavan	Findings write-up	Final findings with exported charts for the report	6h	Docs
Pavan	Test coverage for ETL and SQL views	Add tests for the views and loads that have none	3h	Tech
Pavan	Report draft: sections 5–8	Merge the analysis, implementation, testing and conclusion sections	3h	Docs
Pavan	Support user-testing sessions	Take notes in 2 sessions	2h	Research
Charmiben	Apply testing feedback to the website	Navigation, wording and layout changes from testing	7h	Tech
Charmiben	Final presentation deck	Slide structure, design and visuals for every section	4h	Docs
Charmiben	Demo script and backup recording	Click-by-click demo script and a screen recording to use if the live site fails	4h	Docs

Member	Task	What it covers	Hours	Type
Charmiben	Fix accessibility issues	Fix everything the Week 5 check found	3h	Tech
Charmiben	Support user-testing sessions	Take notes in 2 sessions	2h	Research

Week 8 · Nov 26–Dec 3 — Final report, code submission, presentation, demo

Shared by all: 2h team meetings, 3h presentation rehearsals (3 runs) and 3h final demo. Each member's rows add up to 14h, for 22h in total.


Member	Task	What it covers	Hours	Type
Dhritiben	Reproducibility test	Fresh clone on a clean machine, build with Docker, and confirm every dashboard matches the live site	5h	Tech
Dhritiben	Final report editing and submission	Read the whole report end to end for one voice; fix cross-references and figure numbers; export the PDF and submit	4h	Docs
Dhritiben	Slides: introduction and project management	Motivation, goals and sprint process, with speaker notes	3h	Docs
Dhritiben	Final acceptance review and code-freeze sign-off	Check every Sprint 4 item is done; sign off the Nov 27 code freeze; transfer hosting and repo access to the supervisor	2h	PM
Romit	Tag release and submit code	v1.0 tag, release notes, and the code submission package	3h	Tech

Member	Task	What it covers	Hours	Type
Romit	Final report: formatting and references	Figure and table numbering, captions, reference list in the required style	4h	Docs
Romit	Final edits: pipeline sections	Apply supervisor and teammate comments to the pipeline pages; re-check every number they cite	4h	Docs
Romit	Slides: data pipeline and validation	Pipeline diagram and data-check results, with speaker notes	3h	Docs
Pavan	Freeze dashboards and export fallbacks	Lock dashboards; export PDF and screenshot versions in case the live site fails	5h	Tech
Pavan	Slides: dashboards and findings	One slide per story with its key finding, with speaker notes	4h	Docs
Pavan	Final edits: analysis sections	Apply supervisor and teammate comments; re-check every number against the dashboards	3h	Docs
Pavan	Q&A question bank	20 likely panel questions with agreed answers	2h	Research
Charmiben	Live demo check and fallback video	Test the demo path on the presentation machine and network; final fallback video	6h	Tech
Charmiben	Final slide design	Consistent visuals across all speakers' slides	4h	Docs
Charmiben	Website final content check	Every link, number and page checked	2h	Tech

Member	Task	What it covers	Hours	Type
Charmiben	Final edits: implementation sections	Apply supervisor and teammate comments to the implementation pages	2h	Docs

Balance check

All four members plan 176–177 hours (22 a week, never below 20), and each spends 52–56% of it on technical work.

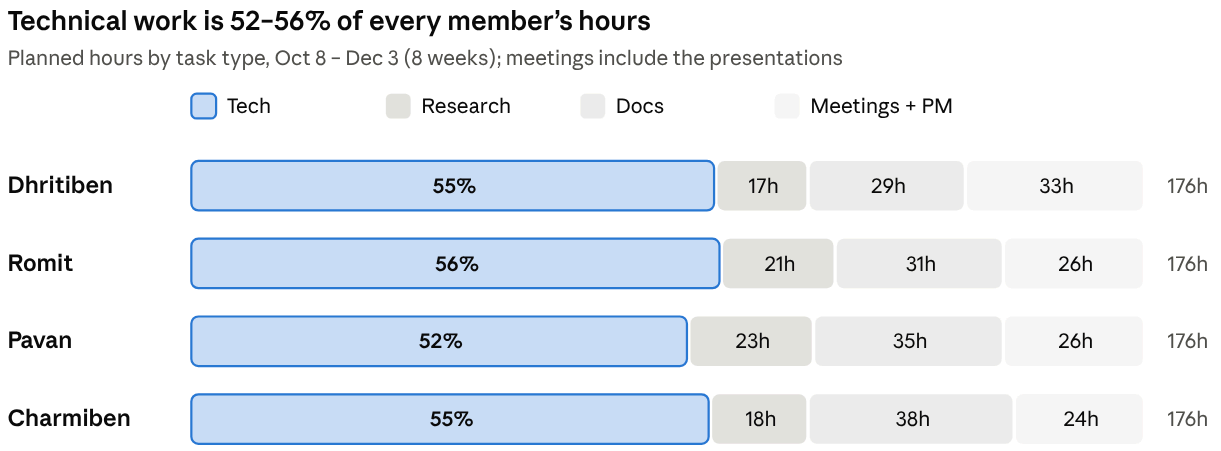

computed from the weekly task tables above · 8 weeks

Everyone also does research, writing and presenting, so each person can explain the whole pipeline at Demo Day. Dhritiben's share now matches the others: she owns deployment and testing work, the status note rotates, and report assembly is split with Pavan and Romit.

Risks and team rules

The biggest risk is hosting Superset for free, so it is tested in Week 2, not left to the end.

Risk	Owner	Early warning	Fallback
Free hosting cannot run Superset (needs about 2–4 GB RAM)	Dhritiben	Week 2 hosting spike fails or crashes	Oracle Cloud Always Free VM, a university server, or React site with exported dashboards plus local live demo
Embedding blocked by auth or CORS	Charmiben	Week 4 prototype not working	Public-role dashboards opened by link from React
Historical CMHC workbooks change structure or zones	Romit	Week 3 harmonizing takes over 9 hours	Keep 5 years instead of 10; note it in methodology
Census (2021) and CMHC (2025) years misread as one period	Pavan	Any SQL join across the two sources	Show side by side at CMA level only; state the years on every chart
Someone falls behind or is sick	Dhritiben	Task not moved to "In review" by Monday	Reviewer for that week takes over; 2h weekly slack covers it

Team rules:

1. Log hours in Jira every week; Dhritiben checks every member is at 20h or more each Wednesday.
2. No task over 9 hours; anything bigger is split before the sprint starts.
3. Nothing is merged to main without one review from another member.
4. Every dashboard number must trace to a source file and row before Week 6 ends.
5. Blocked for more than a day means saying so in Teams the same day.
6. Code freeze is Nov 27; after that, only bug fixes.
